



The Hub Herald

No.32. 21/11/16

Last week was another busy one on site where we saw the student street completed along with the access ramp and concrete apron on the southern side. The cladding progressed further and is almost completed, the roof and cladding progressed on the eastern walkway, inside the remedial work was 99% completed and the old library area was transformed into a study space. We also started the outdoor furniture manufacture, started painting the structure above the soffits black and the planting in the gardens progressed well.

This week we will be completing the exterior cladding, continuing the outdoor furniture manufacture, complete the planting, complete a final clean on the outside and remove all the site fencing. By the end of the week it will no longer look like a construction area.

Next week, we will continue and complete the furniture manufacture.

This will be the last week that the site will look like a building site which is great, we will still be constructing some furniture next week but it will be only in isolated areas and we will not disrupt any of the student or staff movements too much.

I would just like to take this opportunity to thank all the Wintec staff and students for their patience through-out the project, everyone has been very positive and helpful through-out which we really appreciate greatly.

As always please feel free to comment on any actions you feel may compromise safety or security on site in any way via the Wintec Project Manager, Miko Brouwer (miko.brouwer@wintec.ac.nz).



Lance Strawbridge (Hawkins Construction Project Manager)

"Safety is no accident"



The eastern canopy with the cladding and roofing being installed.




The student street completed



Some of the planting completed on the eastern side.



The tree seat furniture progressing.

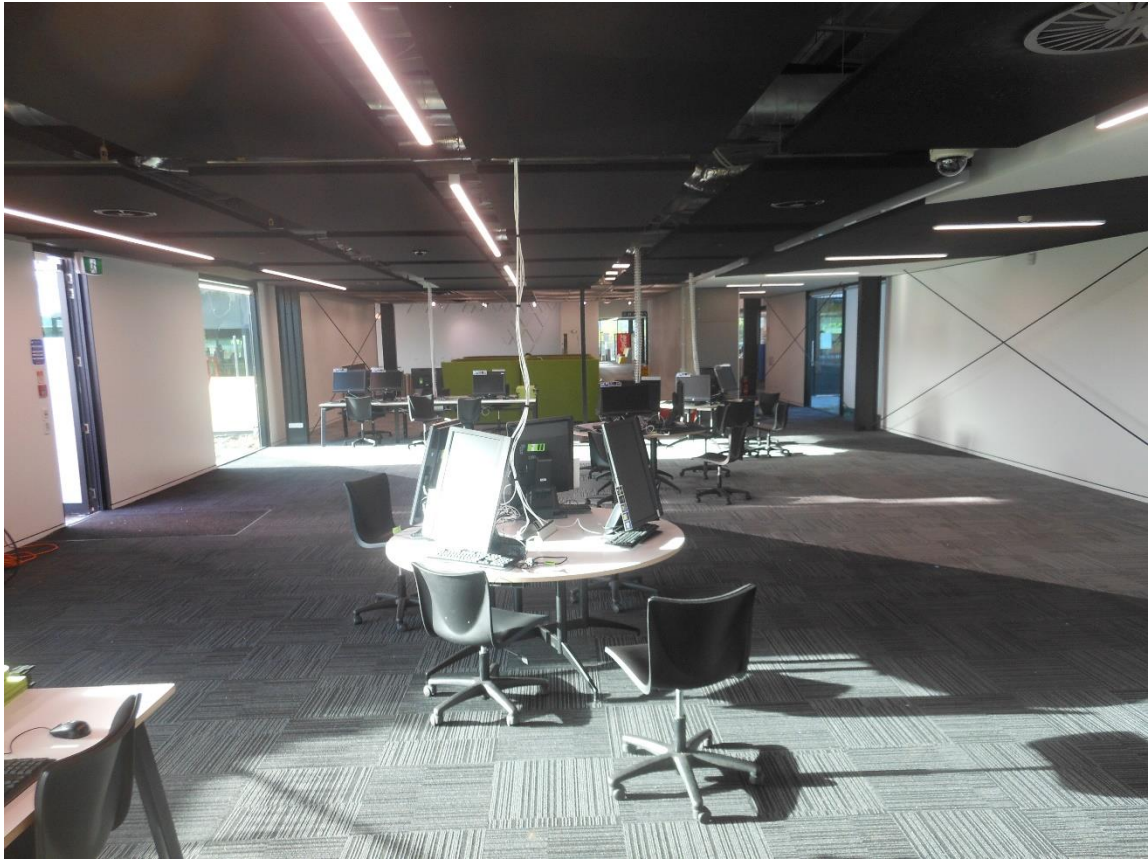

The old library area up-graded to a modern study space



The new ramp concrete and planting completed
